







































ID	Task Name	Duration	Start	Finish	% Complete	Predecessors	Successors	2016	
								Qtr 1, 2016	Qtr 2, 2016
								Jan	Feb
1	TAVARES - CRA STORM IMPROVEMENTS - PREBID	448.19 days	Thu 2/4/16	Tue 10/24/17	15%				
2	Preconstruction Activities	162.19 days	Thu 2/4/16	Mon 9/19/16	99%				
10	Contract Duration	322 days	Mon 8/1/16	Tue 10/24/17	7%				
13	Submittals	85 days	Fri 6/3/16	Fri 9/30/16	27%				
32	Material Procurement	128.5 days	Fri 9/2/16	Thu 3/2/17	0%				
35	Mobilization	27 days	Fri 8/26/16	Mon 10/3/16	7%				
41	STORM WATER POND CONSTRUCTION	132.31 days	Tue 9/27/16	Thu 3/30/17	0%				
55	INSTALL STORMWATER, UTILITIES & ROADWORK	253 days	Tue 10/4/16	Thu 9/21/17	0%				
56	Phase 1 (Sinclair to Ruby, Ruby to Joanna)	98 days	Tue 10/4/16	Thu 2/16/17	0%				
64	Phase 1A (Boat Ramp Storm and Jack & Bore)	26 days	Wed 11/23/16	Wed 12/28/16	0%				


Project: Tavares Storm Improvements Condensed Schedule 8-26

Task		Manual Summary Rollup	
Split		Manual Summary	
Milestone		Start-only	
Summary		Finish-only	
Project Summary		External Tasks	
Inactive Task		External Milestone	
Inactive Milestone		Deadline	
Inactive Summary		Progress	
Manual Task		Manual Progress	
Duration-only			


ID	Task Name	Duration	Start	Finish	% Complete	Predecessors	Successors	2016	
								Qtr 1, 2016	Jan
70	Phase 1B (Joanna)	33 days	Thu 12/22/16	Mon 2/6/17	0%				
78	Phase 2A (Joanna to New Hampshire 23+00)	17 days	Mon 2/6/17	Tue 2/28/17	0%				
84	Phase 2B (New Hampshire-Ruby Intersection to J&B)	26 days	Wed 3/1/17	Wed 4/5/17	0%				
91	Phase 3A (New Hampshire to Rockingham 26+50)	18 days	Thu 4/6/17	Mon 5/1/17	0%				
99	Phase 3B (Rockingham Intersection)	19 days	Tue 5/2/17	Fri 5/26/17	0%				
107	Phase 4A (Rockinghm to St. Clair 30+25)	15 days	Mon 5/29/17	Fri 6/16/17	0%				
114	Phase 4B (St. Clair Intersection)	14 days	Mon 6/19/17	Thu 7/6/17	0%				
121	Phase 5 (Concrete Flatwork, Pavers and Brick)	55 days	Fri 7/7/17	Thu 9/21/17	0%				
127	Substantial Completion	1 day	Fri 9/22/17	Fri 9/22/17	0%	126	129,130,132,133		
128	Closeout Phase	20 days	Mon 9/25/17	Fri 10/20/17	0%				

Project: Tavares Storm Improvements Condensed Schedule 8-26

Task		Manual Summary Rollup	
Split		Manual Summary	
Milestone		Start-only	
Summary		Finish-only	
Project Summary		External Tasks	
Inactive Task		External Milestone	
Inactive Milestone		Deadline	
Inactive Summary		Progress	
Manual Task		Manual Progress	
Duration-only			

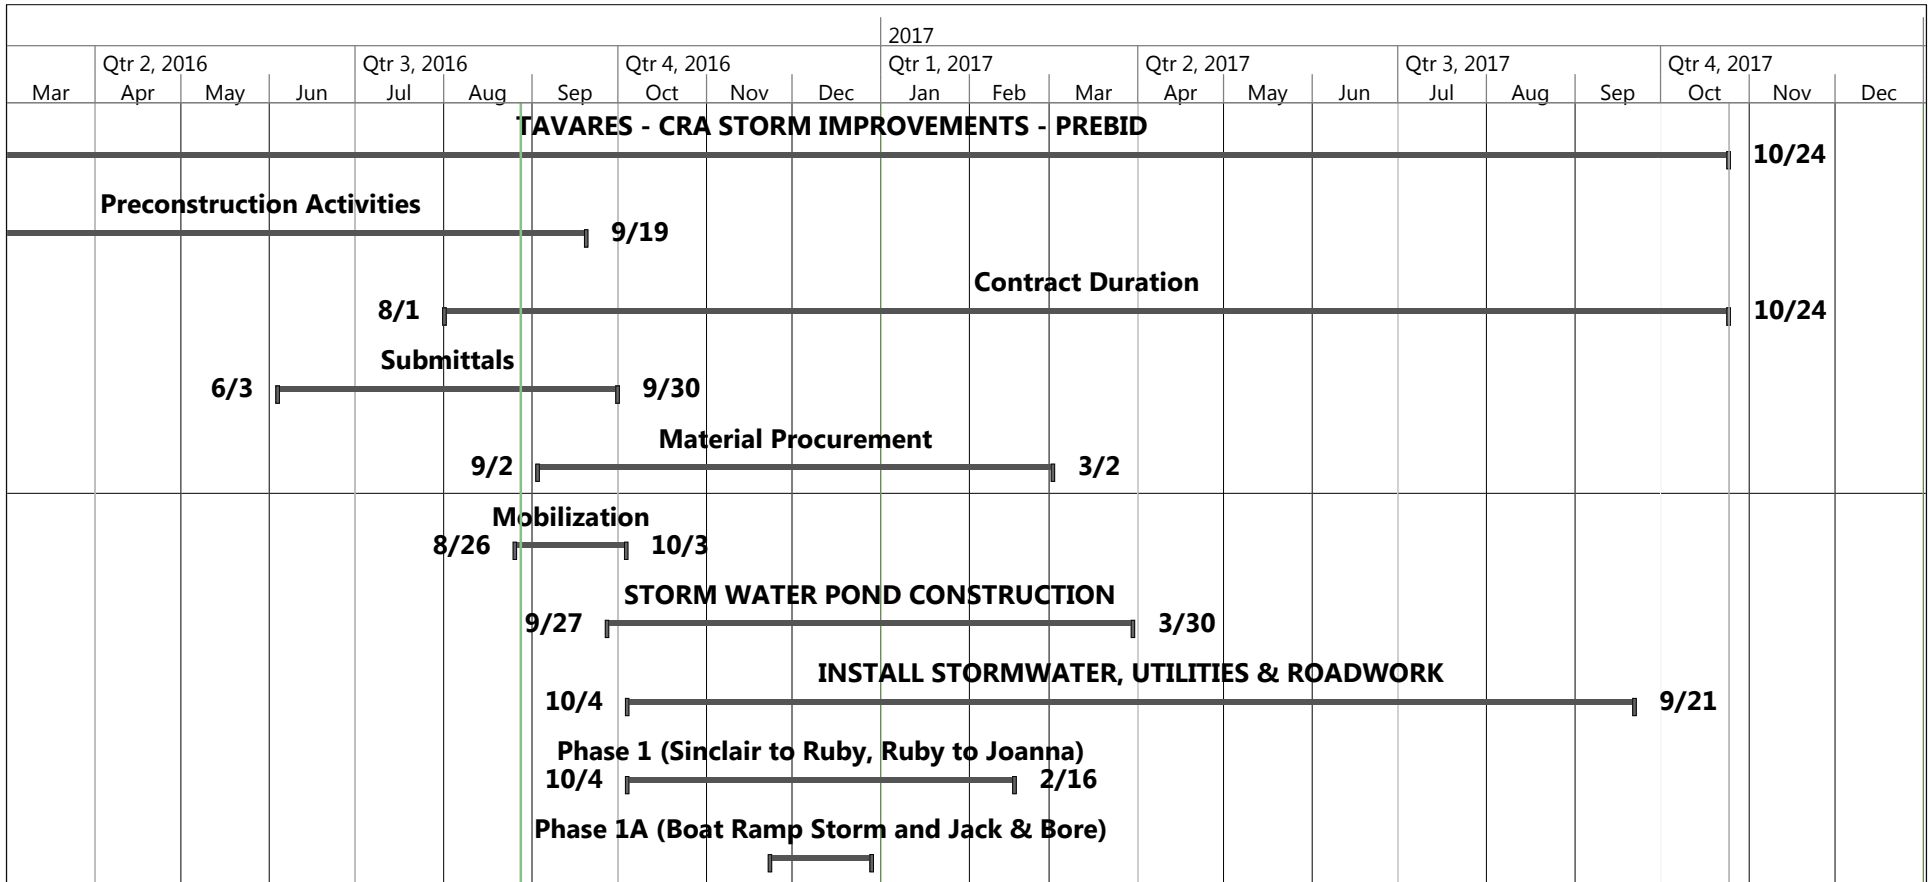

Project: Tavares Storm Improvements Condensed Schedule 8-26	Task		Manual Summary Rollup	
	Split		Manual Summary	
	Milestone		Start-only	
	Summary		Finish-only	
	Project Summary		External Tasks	
	Inactive Task		External Milestone	
	Inactive Milestone		Deadline	
	Inactive Summary		Progress	
	Manual Task		Manual Progress	
	Duration-only			

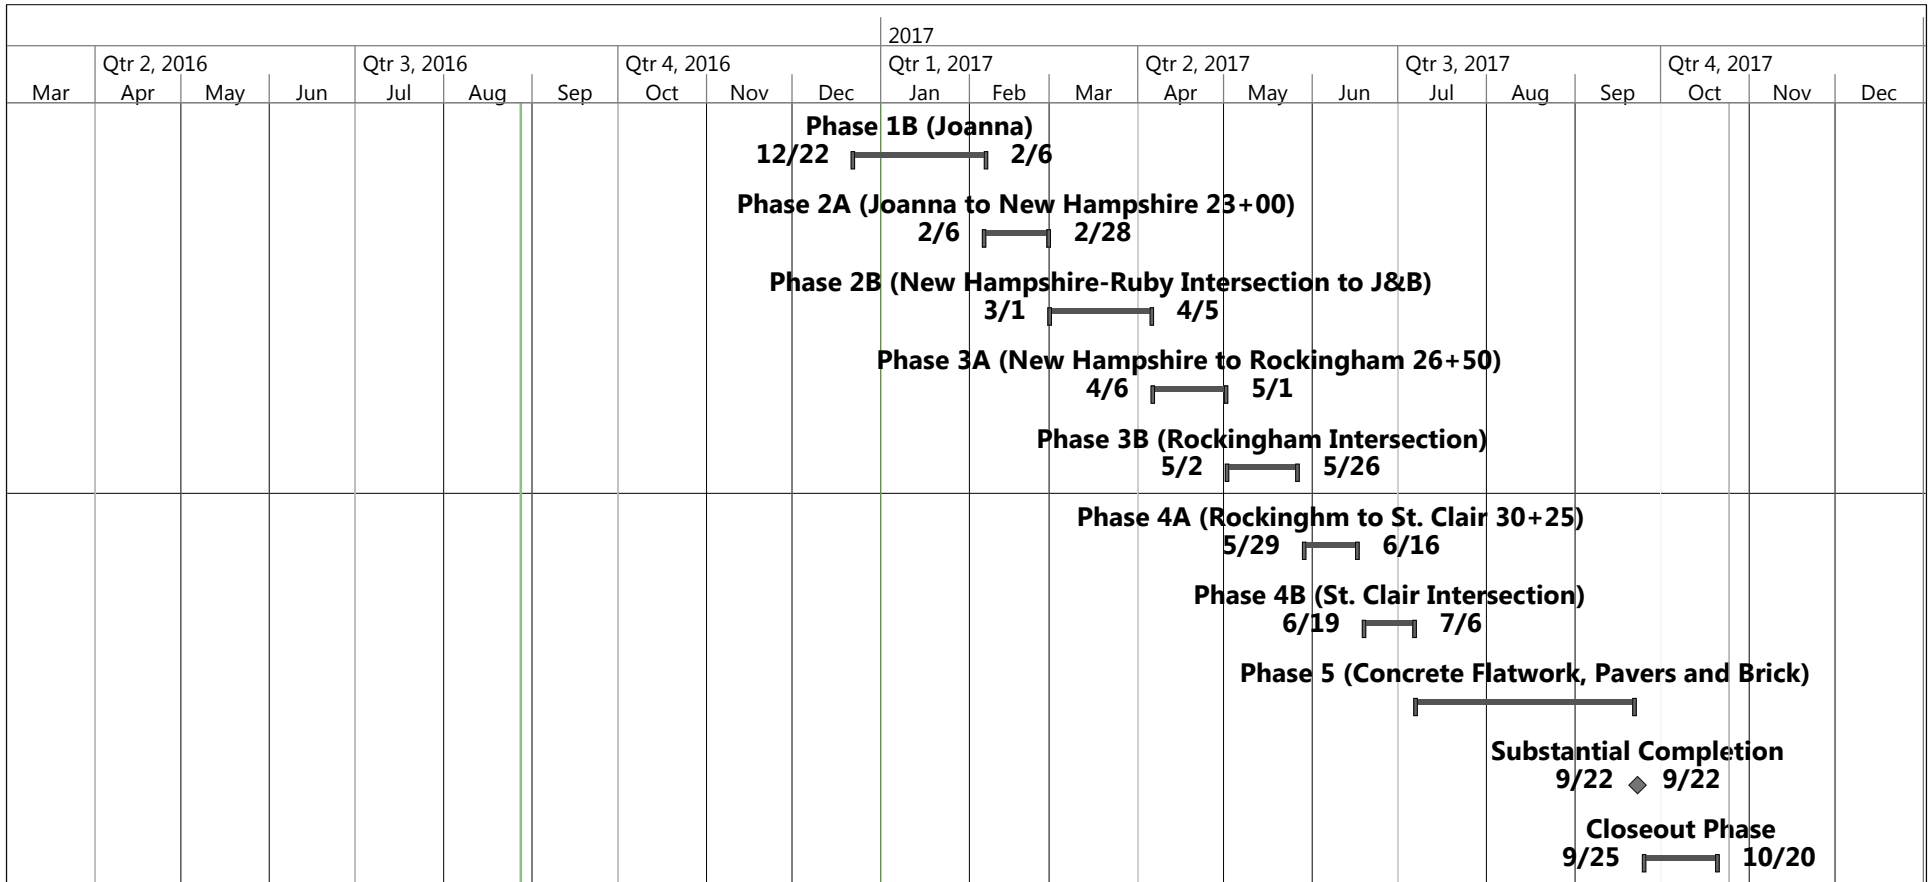

Project: Tavares Storm Improvements Condensed Schedule 8-26	Task		Manual Summary Rollup	
	Split		Manual Summary	
	Milestone		Start-only	
	Summary		Finish-only	
	Project Summary		External Tasks	
	Inactive Task		External Milestone	
	Inactive Milestone		Deadline	
	Inactive Summary		Progress	
	Manual Task		Manual Progress	
	Duration-only			
